



West Broadway Urban Village
 Infrastructure Improvements Project
 City of Seaside
 Project No. 2016-76
 Federal No. ATPL-5316 (007)

Report No: **3**
 Date: **06/06/17**
 Day: **Tuesday**
 Shift Hours: Start **0800**
 Stop **1600**

- | | | |
|---|--|--|
| <input type="checkbox"/> Material Source Inspection | <input type="checkbox"/> Certificate Of Compliance | <input type="checkbox"/> Employee Interview |
| <input type="checkbox"/> Material Inspected and Released on Job | <input type="checkbox"/> Acceptance Test (IA) | <input checked="" type="checkbox"/> Photos |
| <input checked="" type="checkbox"/> No Quality Documents Required | <input type="checkbox"/> Quality Documents Submitted | <input type="checkbox"/> Tentative Agreement |

ASSISTANT RESIDENT ENGINEER'S DAILY INSPECTION REPORT Page 1 of 2

HOURS - ITEM No. or CCO No.

M = Monterey Peninsula Engineering
 SA = Stripe Alot

	Traffic Control System	Temporary Railing (Type K)	Temporary Traffic Stripe (Paint)	Elsewhere / Idle
--	------------------------	----------------------------	----------------------------------	------------------

WEATHER
 AM 52°F +/-
 PM 60°F +/-
 Mostly Cloudy

PRECIP
 wind: 0-20 mph

Con	NO.	EQUIPMENT / MAKE	8	15	9				LABOR - TRADE / NAME
M		Backhoe, Case 590	8	6					Johnson, BJ; Foreman
M		Flatbed Truck, 12-20K# GVW	4	4					Lucas, Justin; laborer
M		3 Axle Dump Truck		8					Zamora, Jose; laborer
M		Flatbed Truck, 12-20K# GVW		8					Gayfan, Gerardo; laborer
M		Excavator, Deere 225C							Bulmaro-Reyes, Chino; operator
M		Pick Up							Hopkins, Darin; laborer
SA		Pick Up			3		5		Haisch, Ken; striper
SA		Trailer			3		5		Upson, Eric; striper


MPE placed temporary K rail on west Broadway from Del Monte to Fremont Blvds. Temporary striping/markings were done at intersections as follows: directing traffic to the single open westbound lane and to add stops at previously free travel intersections; and to prohibit turns into the construction work zone on the south side of Broadway. Traffic control for detours included installation of the following: CMS on Del Monte Blvd (west of Del Rey Oaks); nd CMS on Del Monte for southbound traffic, north of the Clementina detour. Sunset Pacific performed trucking for K rail delivery.

Today's Qtys (approx.)

Kathryn Lett, Asst Res Engineer
 Inspector

ASSISTANT RESIDENT ENGINEER'S DAILY INSPECTION REPORT:

PHOTOS

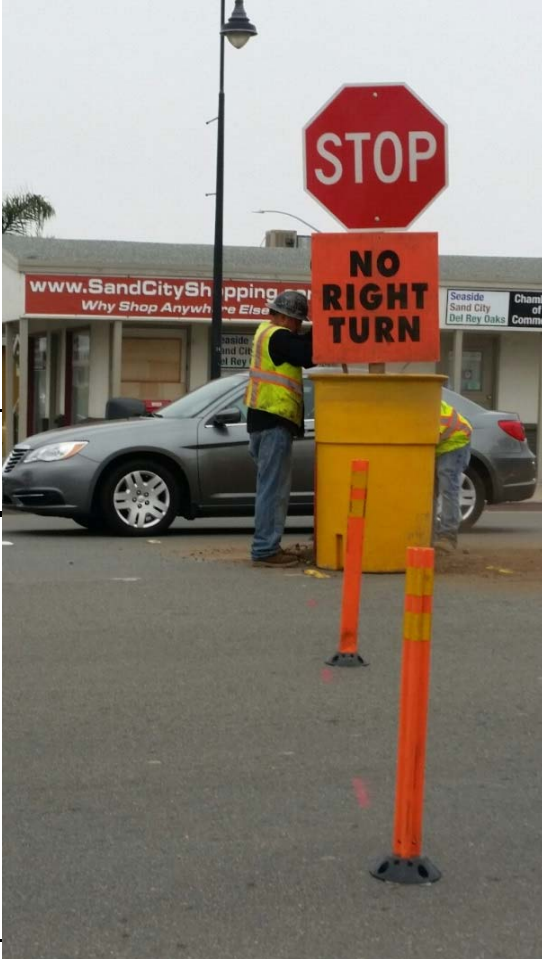

Intersection: prohibit right turn into construction work zone eastbound



Traffic control for K rail placement



West Broadway closure at Del Monte Ave

Kathryn Lett

Inspector
