




West Broadway Urban Village  
Infrastructure Improvements Project  
City of Seaside  
Project No. 2016-76  
Federal No. ATPL-5316 (007)

Report No: **16**  
Date: **06/23/17**  
Day: **Friday**  
Shift Hours: Start **0800**  
Stop **1600**

- Material Source Inspection
- Certificate Of Compliance
- Employee Interview
- Material Inspected and Released on Job
- Acceptance Test (IA)
- Photos
- No Quality Documents Required
- Quality Documents Submitted
- Tentative Agreement

**HOURS - ITEM No. or CCO No.**

M = Monterey Peninsula Engineering  
SA = Stripe Alot

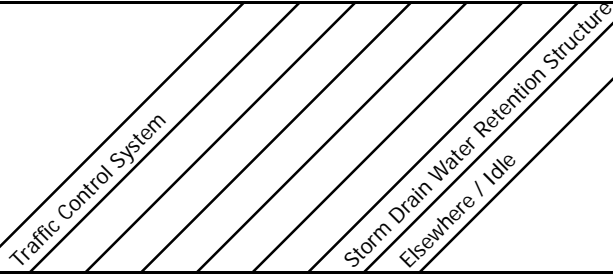

**WEATHER**  
AM 52°F +/-  
PM 76°F +/-  
Clear  
**PRECIP**  
wind: 0-15 mph

Con	NO.	EQUIPMENT / MAKE	8					61		LABOR - TRADE / NAME
M		Bobcat T190 with broom atch						1	7	Lucas, Justin; laborer
M		Pick Up	3					2	3	Lucas, Justin; laborer
M		Excavator, Deere 225C						8		Bulmaro-Reyes, Chino; operator
M		Bobcat T190						2	6	Pack, John; laborer
M		Excavator, Kobelco SK220						8		Honeycut, Ritchie; foreman
M		Fork Lift						2	6	Pack, John; laborer
M		Pick Up						4	4	Pack, John; laborer
M		Pick Up						8		Sandoval, Manual J; laborer
M		Water Tank Trailer						2	6	Lucas, Justin; laborer
M		Loader, Deere 644J							8	

MPE began excavating at Infiltrator #3 and continued removing sheet pile from Infiltrator #2 site.  
Traffic control detours and devices in place and functioning. Dust control using water sprayed on rock, sand, and grindings throughout the day.

**Today's Qtys (approx.)**

Trucking by Bunker and Sons.

**Kathryn Lett, Asst Res Engineer**  
**Inspector**
