



West Broadway Urban Village
 Infrastructure Improvements Project
 City of Seaside
 Project No. 2016-76
 Federal No. ATPL-5316 (007)

Report No: **50**
 Date: **08/15/17**
 Day: **Tuesday**
 Shift Hours: Start **0700**
 Stop **1530**

- | | | |
|---|--|--|
| <input type="checkbox"/> Material Source Inspection | <input type="checkbox"/> Certificate Of Compliance | <input type="checkbox"/> Employee Interview |
| <input type="checkbox"/> Material Inspected and Released on Job | <input type="checkbox"/> Acceptance Test (IA) | <input checked="" type="checkbox"/> Photos |
| <input checked="" type="checkbox"/> No Quality Documents Required | <input type="checkbox"/> Quality Documents Submitted | <input type="checkbox"/> Tentative Agreement |

ASSISTANT RESIDENT ENGINEER'S DAILY INSPECTION REPORT Page 1 of 2

HOURS - ITEM No. or CCO No.

M = Monterey Peninsula Engineering
 SA = Stripe Alot
 CC = Central Coast Surveyors
 DJ Kirkpatrick Sawcutting = KS
 Penhall = P

WEATHER
 AM 60°F +/-
 PM 68°F +/-
 Overcast

PRECIP
 wind: 0-15 mph

Con	NO.	EQUIPMENT / MAKE	8	59	61					LABOR - TRADE / NAME
M		Excavator, Deere 225D			1				7	Bulmaro-Reyes, Chino; operator
M		Loader, DEERE 544K		2					6	Bulmaro-Reyes, Chino; operator
		private auto		5					3	Bulmaro-Reyes, Chino; operator
M		Pick Up		6	1				1	Sandoval, Manual J; laborer
M		Water Truck, 2200 gallon			1				7	
M		Excavator, Deere 225D		5					3	Honeycut, Ritchie; foreman
M		Pick Up	1	2					5	Honeycut, Ritchie; foreman
M		Excavator, Kobelco SK220							8	
M		Backhoe, Case 590							8	
M		Gradall, Sky Trak							8	
M		Dump Truck, two axle							8	
M		Grader, Cat 140H							8	

MPE completed the sheet pile placement and backfill at Infiltrator #1 (Hillsdale St) for the weir and HDS installation. Next, MPE closed the Calaveras Street intersection for excavation and placement of the storm drain manhole, 6e. Traffic control devices and detours were functioning in place. Temporary fence was relocated to secure the Calaveras work area; "road closed" signs placed.

Today's Qtys (approx.)

Item 6, Temporary Fence: 9 panels relocated to Calaveras = 54 LF.

Kathryn Lett, Asst RE
 Inspector



West Broadway Urban Village
 Infrastructure Improvements Project
 City of Seaside
 Project No. 2016-76
 Federal No. ATPL-5316 (007)

Report No: **50**
 Date: **08/15/17**
 Day: **Tuesday**
 Shift Hours: Start **0700**
 Stop **1530**



ASSISTANT RESIDENT ENGINEER'S DAILY INSPECTION REPORT:

Page 2 of 2

PHOTOS



Placement of drainage structure, 6e

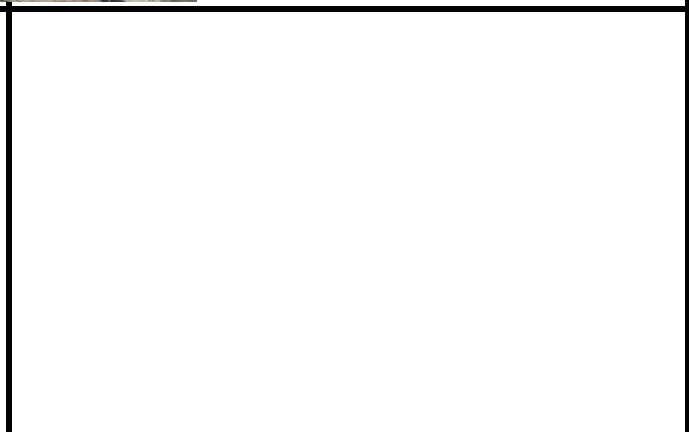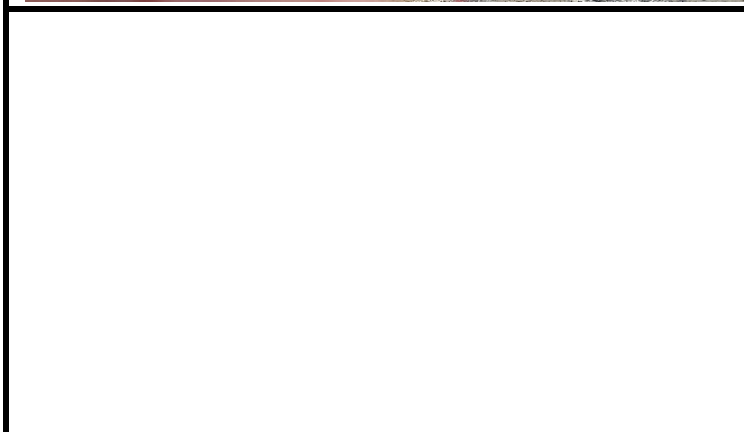

Kathryn Lett
 Inspector
